

TIER 2 ENTRY IMPROVEMENTS CROWN VALLEY PARK

JOB PROGRESS/SCHEDULE ASSESSMENT AS OF		2/24/2017
Notice To Proceed:	7/4/2016	
Contract Working Days:	230	
Time Extensions:	0	
Revised Working Days:	0	
Total Days to Date:	164	
Total Days Remaining:	66	
Percent Complete	71.3%	
Project Completion:	6/7/2017	

***** WEEKLY PROJECT IMAGES *****



Bridge Pilaster Pot Drainage



Concrete Pilasters

**TIER 2 ENTRY IMPROVEMENTS
CROWN VALLEY PARK**




8" Reclaimed Water Bridge Crossing



Concrete Pour For Bridge Pilasters




Raise In Place Reclaimed Water Meter & Vault

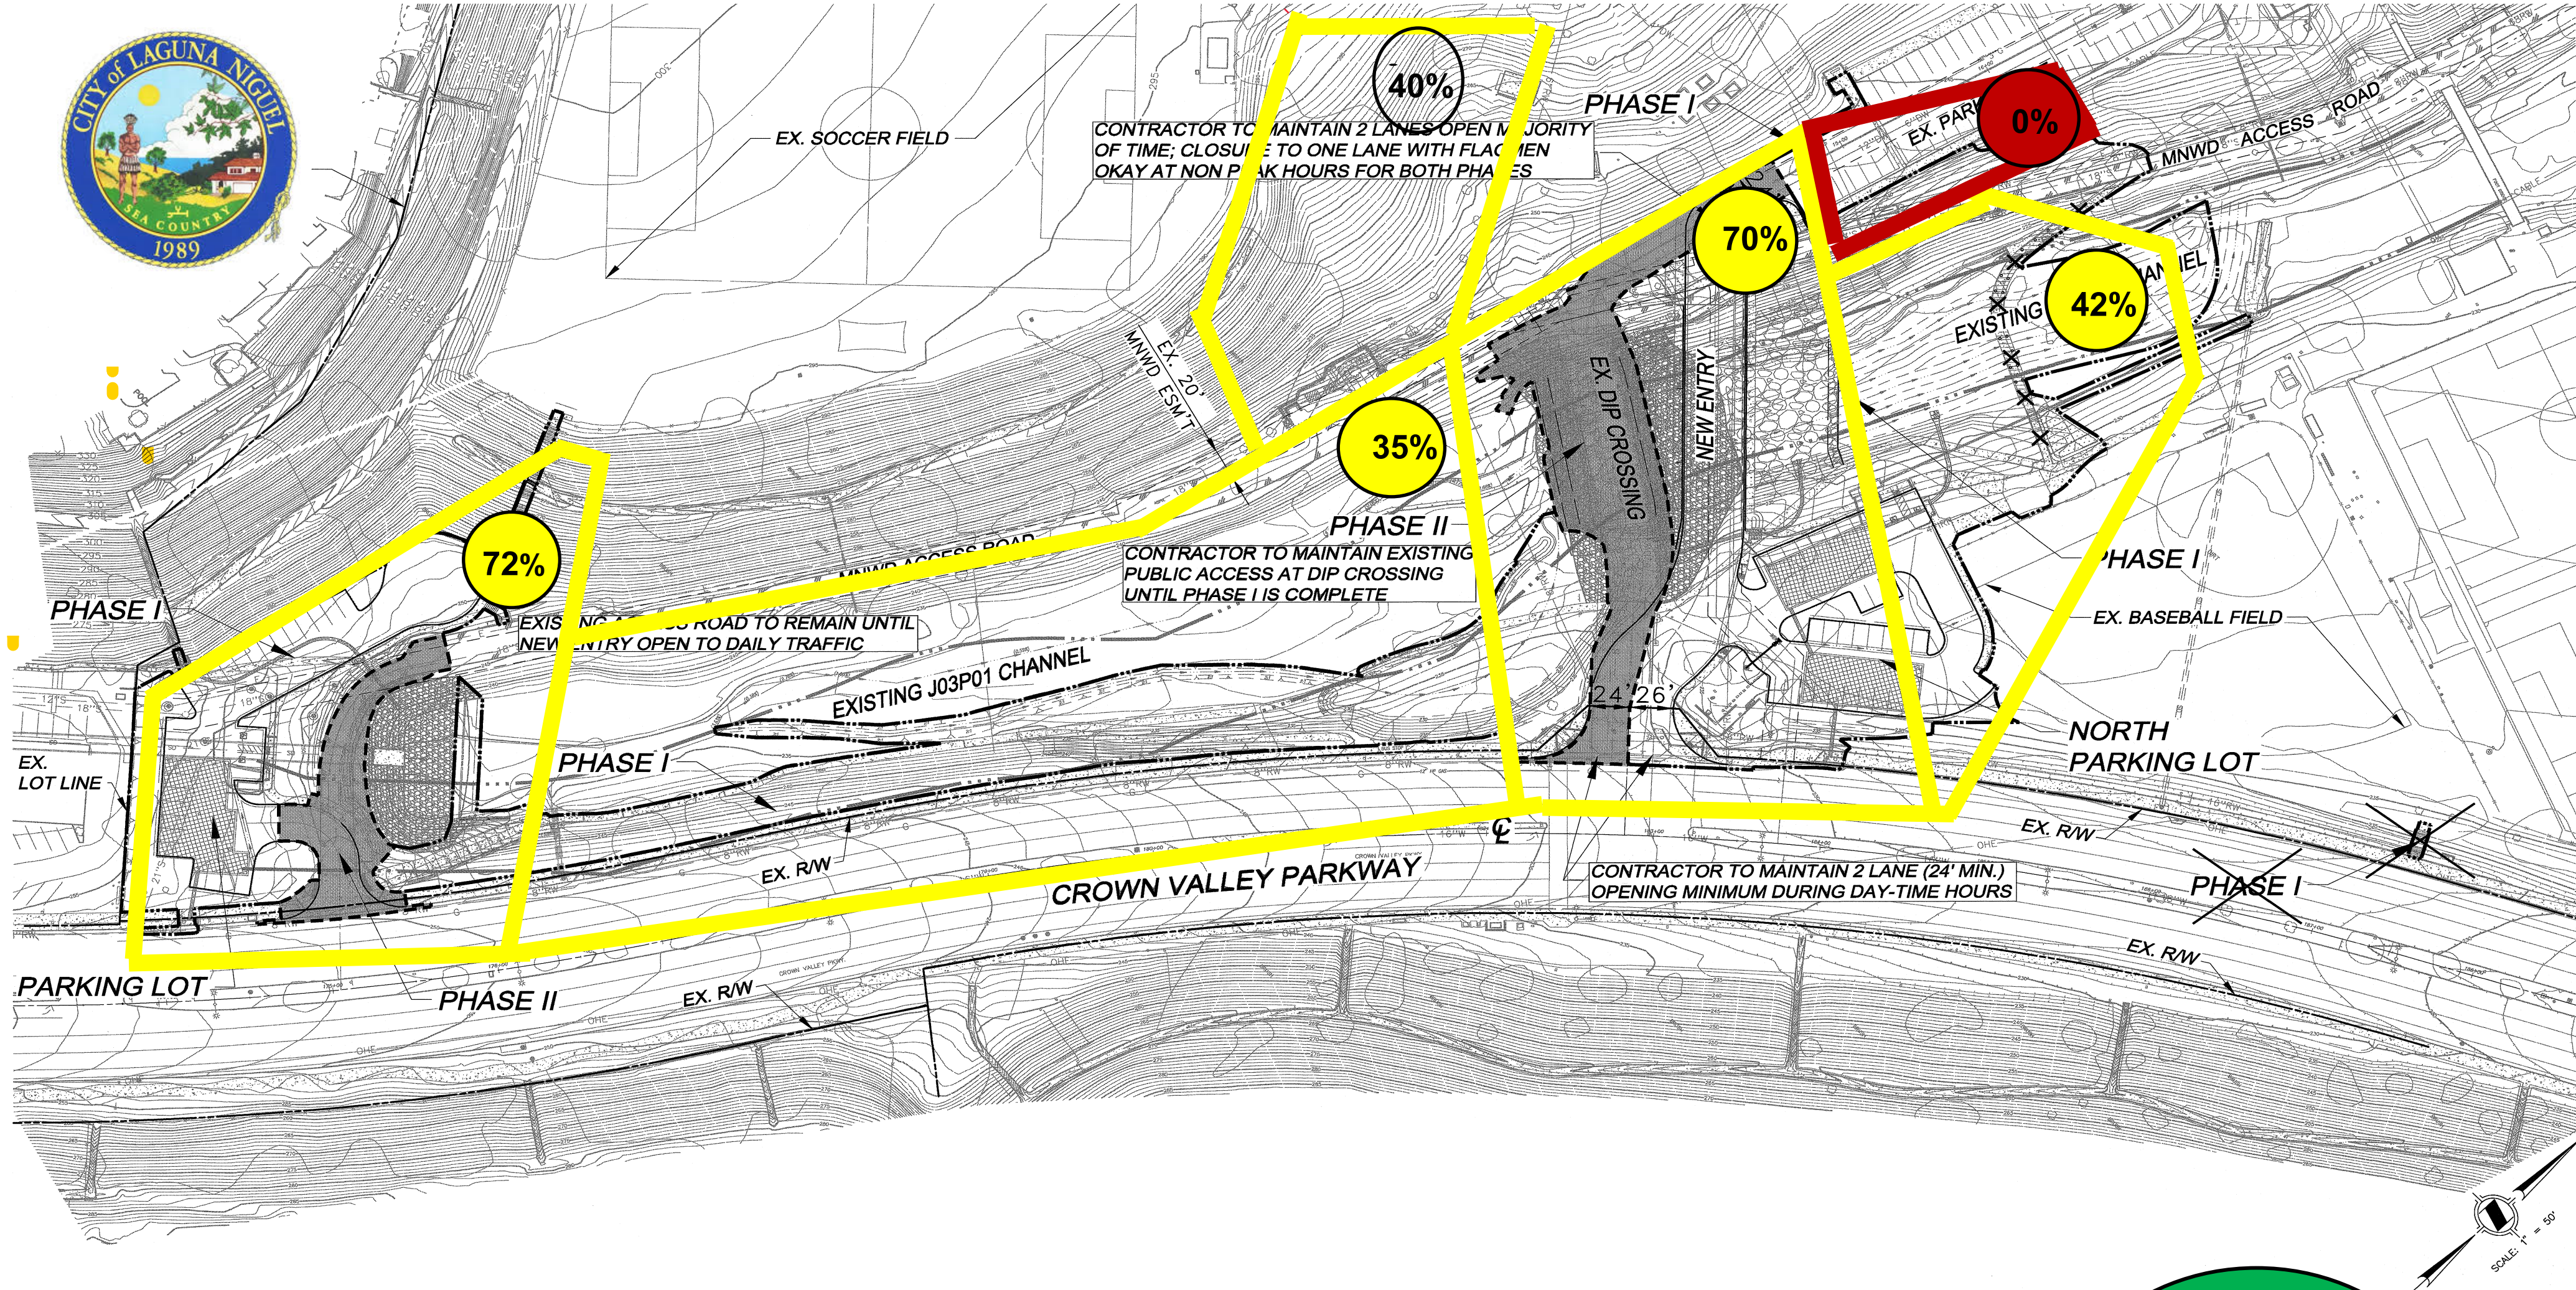

CROWN VALLEY PARK – TIER 2 CONSTRUCTION PROGRESS CHART



CONSTRUCTION PENDING	0% Complete	Construction Start July 5, 2016
CONSTRUCTION UNDERWAY	1% - 99% Complete	 WEEK 33
CONSTRUCTION COMPLETED	100% Complete	Construction Completion June 7, 2017

Feb 24, 2017

Your Park is
69.1%
Complete
