

TIER 2 ENTRY IMPROVEMENTS CROWN VALLEY PARK

JOB PROGRESS/SCHEDULE ASSESSMENT AS OF 1/20/2017

Notice To Proceed:	7/4/2016
Contract Working Days:	230
Time Extensions:	0
Revised Working Days:	0
Total Days to Date:	138
Total Days Remaining:	92
Percent Complete	60.0%
Project Completion:	6/7/2017

******* WEEKLY PROJECT IMAGES *******



Backfilling Arch & Arch Footings



Bridge Arch Wall Bracing

**TIER 2 ENTRY IMPROVEMENTS
CROWN VALLEY PARK**




South Entrance Monument Footing Pour



South Parking Lot Lighting Conduit




North Channel Storm Flow

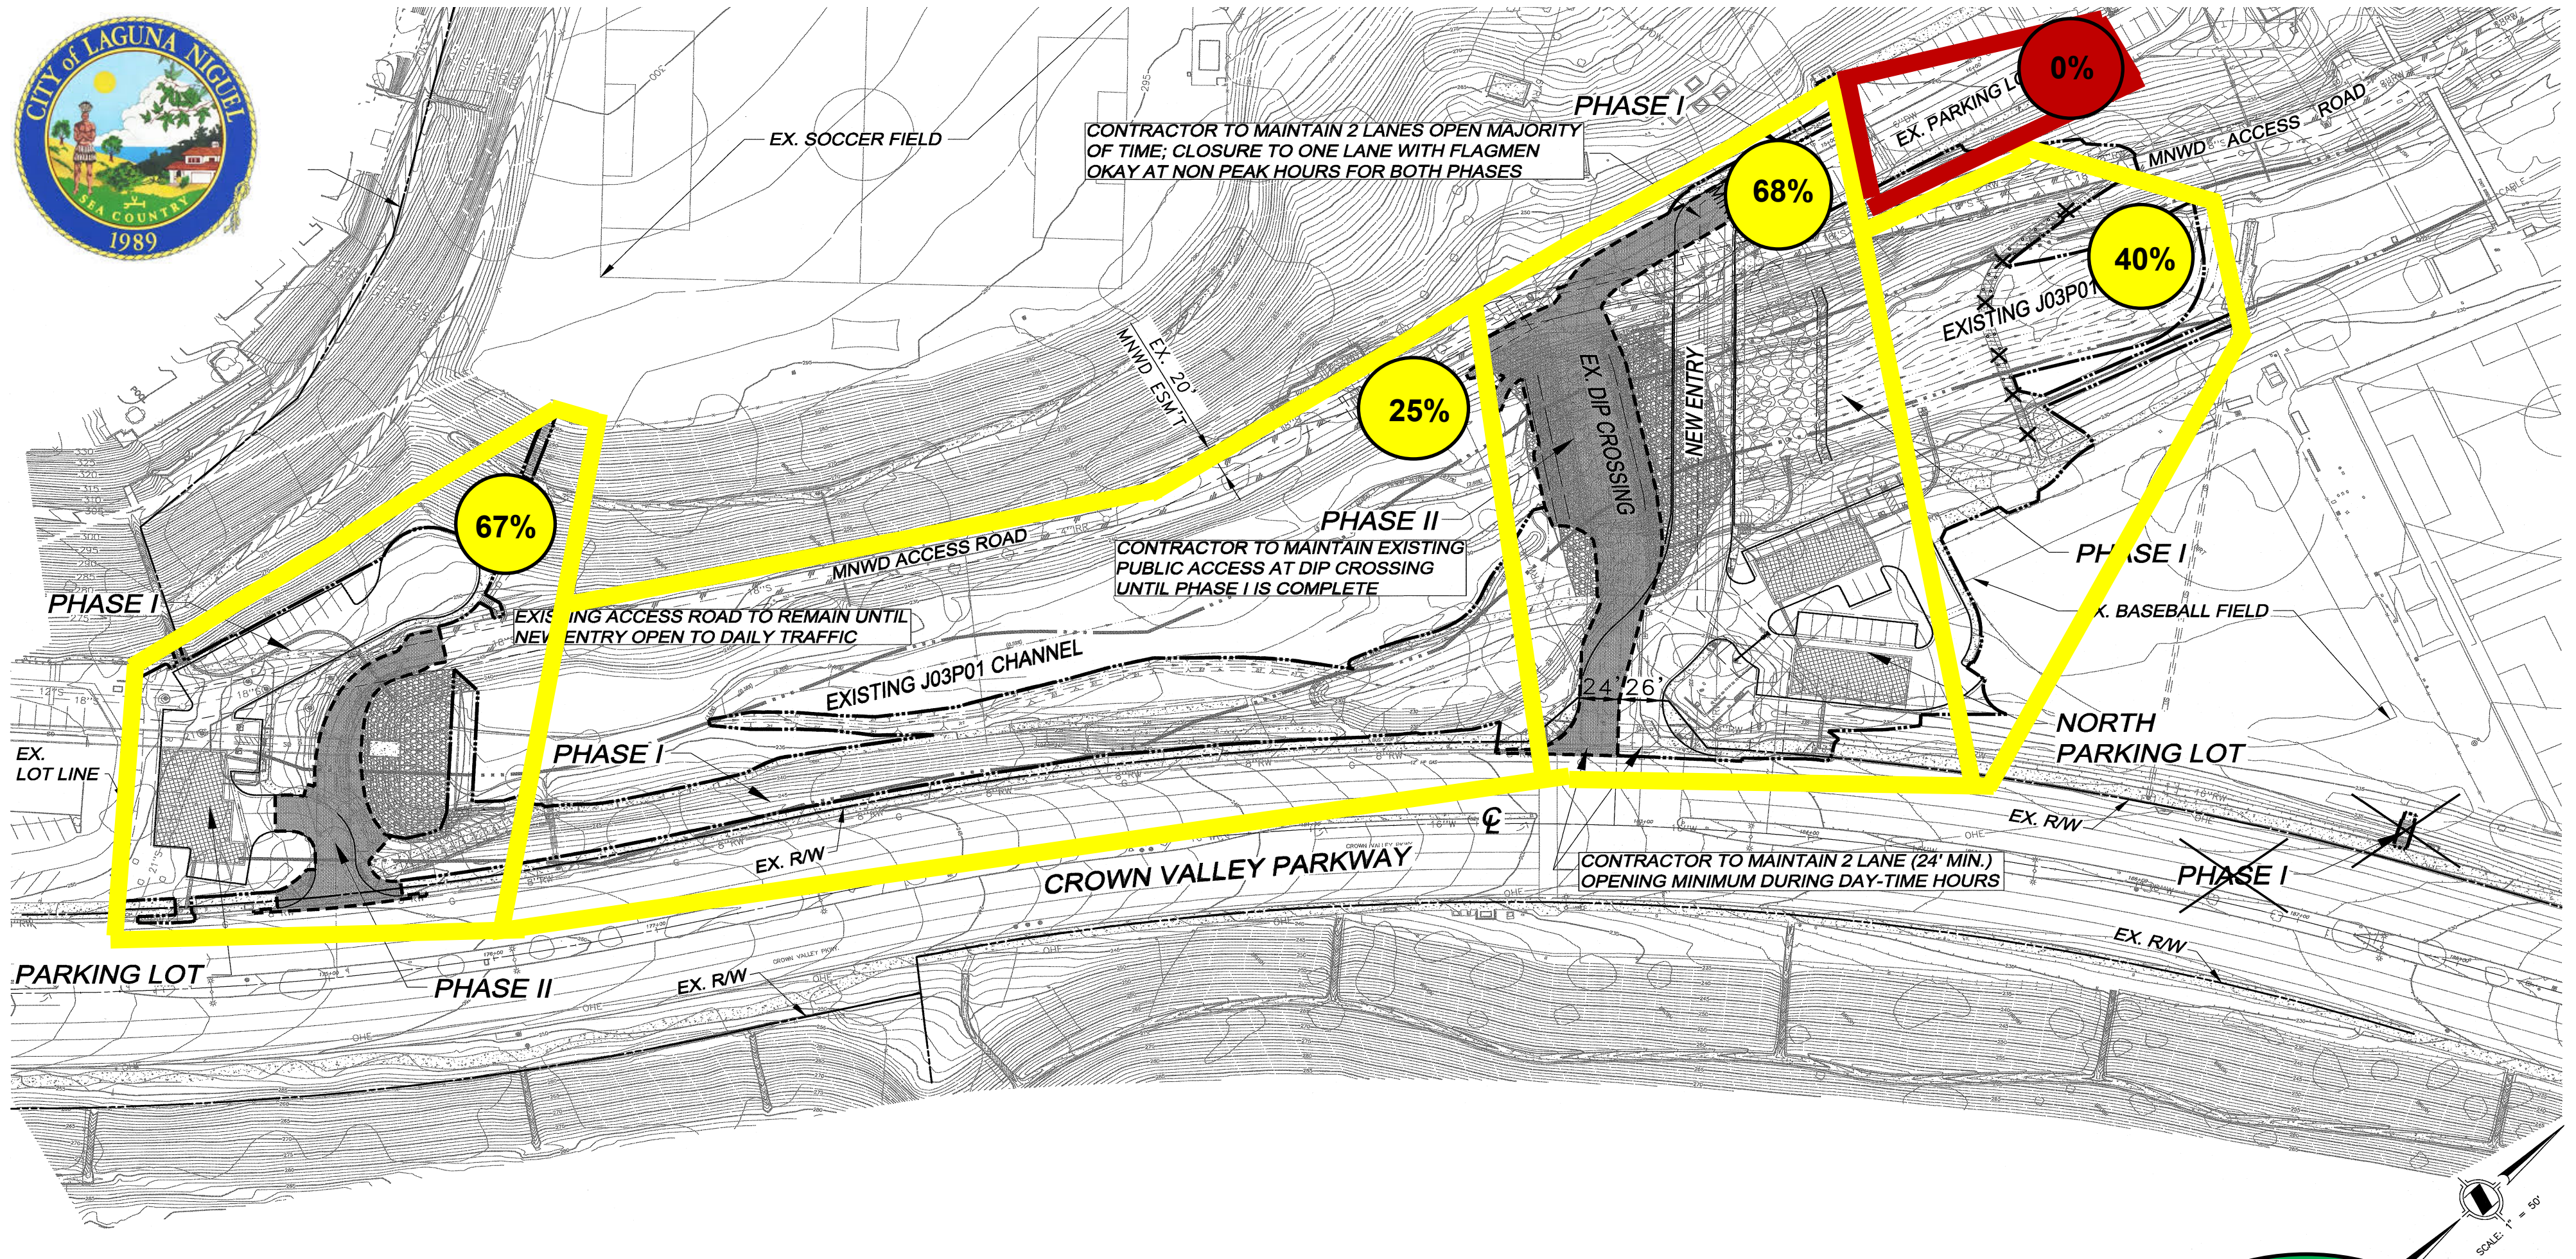

CROWN VALLEY PARK – TIER 2 CONSTRUCTION PROGRESS CHART



CONSTRUCTION PENDING	0% Complete	Construction Start July 5, 2016
CONSTRUCTION UNDERWAY	1% - 99% Complete	 WEEK 28
CONSTRUCTION COMPLETED	100% Complete	Construction Completion June 7, 2017

Jan. 20, 2016

Your Park is
60.0%
Complete
