

TIER 2 ENTRY IMPROVEMENTS CROWN VALLEY PARK

JOB PROGRESS/SCHEDULE ASSESSMENT AS OF	4/28/2017
Notice To Proceed:	7/4/2016
Contract Working Days:	230
Time Extensions:	0
Revised Working Days:	245
Rain Days Used	15
Total Days to Date:	193
Total Days Remaining:	52
Percent Complete	78.8%
Project Completion:	6/29/2017

***** WEEKLY PROJECT IMAGES *****



South Parking Lot Light Pole Foundation and Pull Box



North Parking Lot Base Grading

**TIER 2 ENTRY IMPROVEMENTS
CROWN VALLEY PARK**




New 8" RW Service Connection Installation Preparation



South Parking lot Landscape Planter Grading & Clean Up




Easement/Trail Paving Base Installed

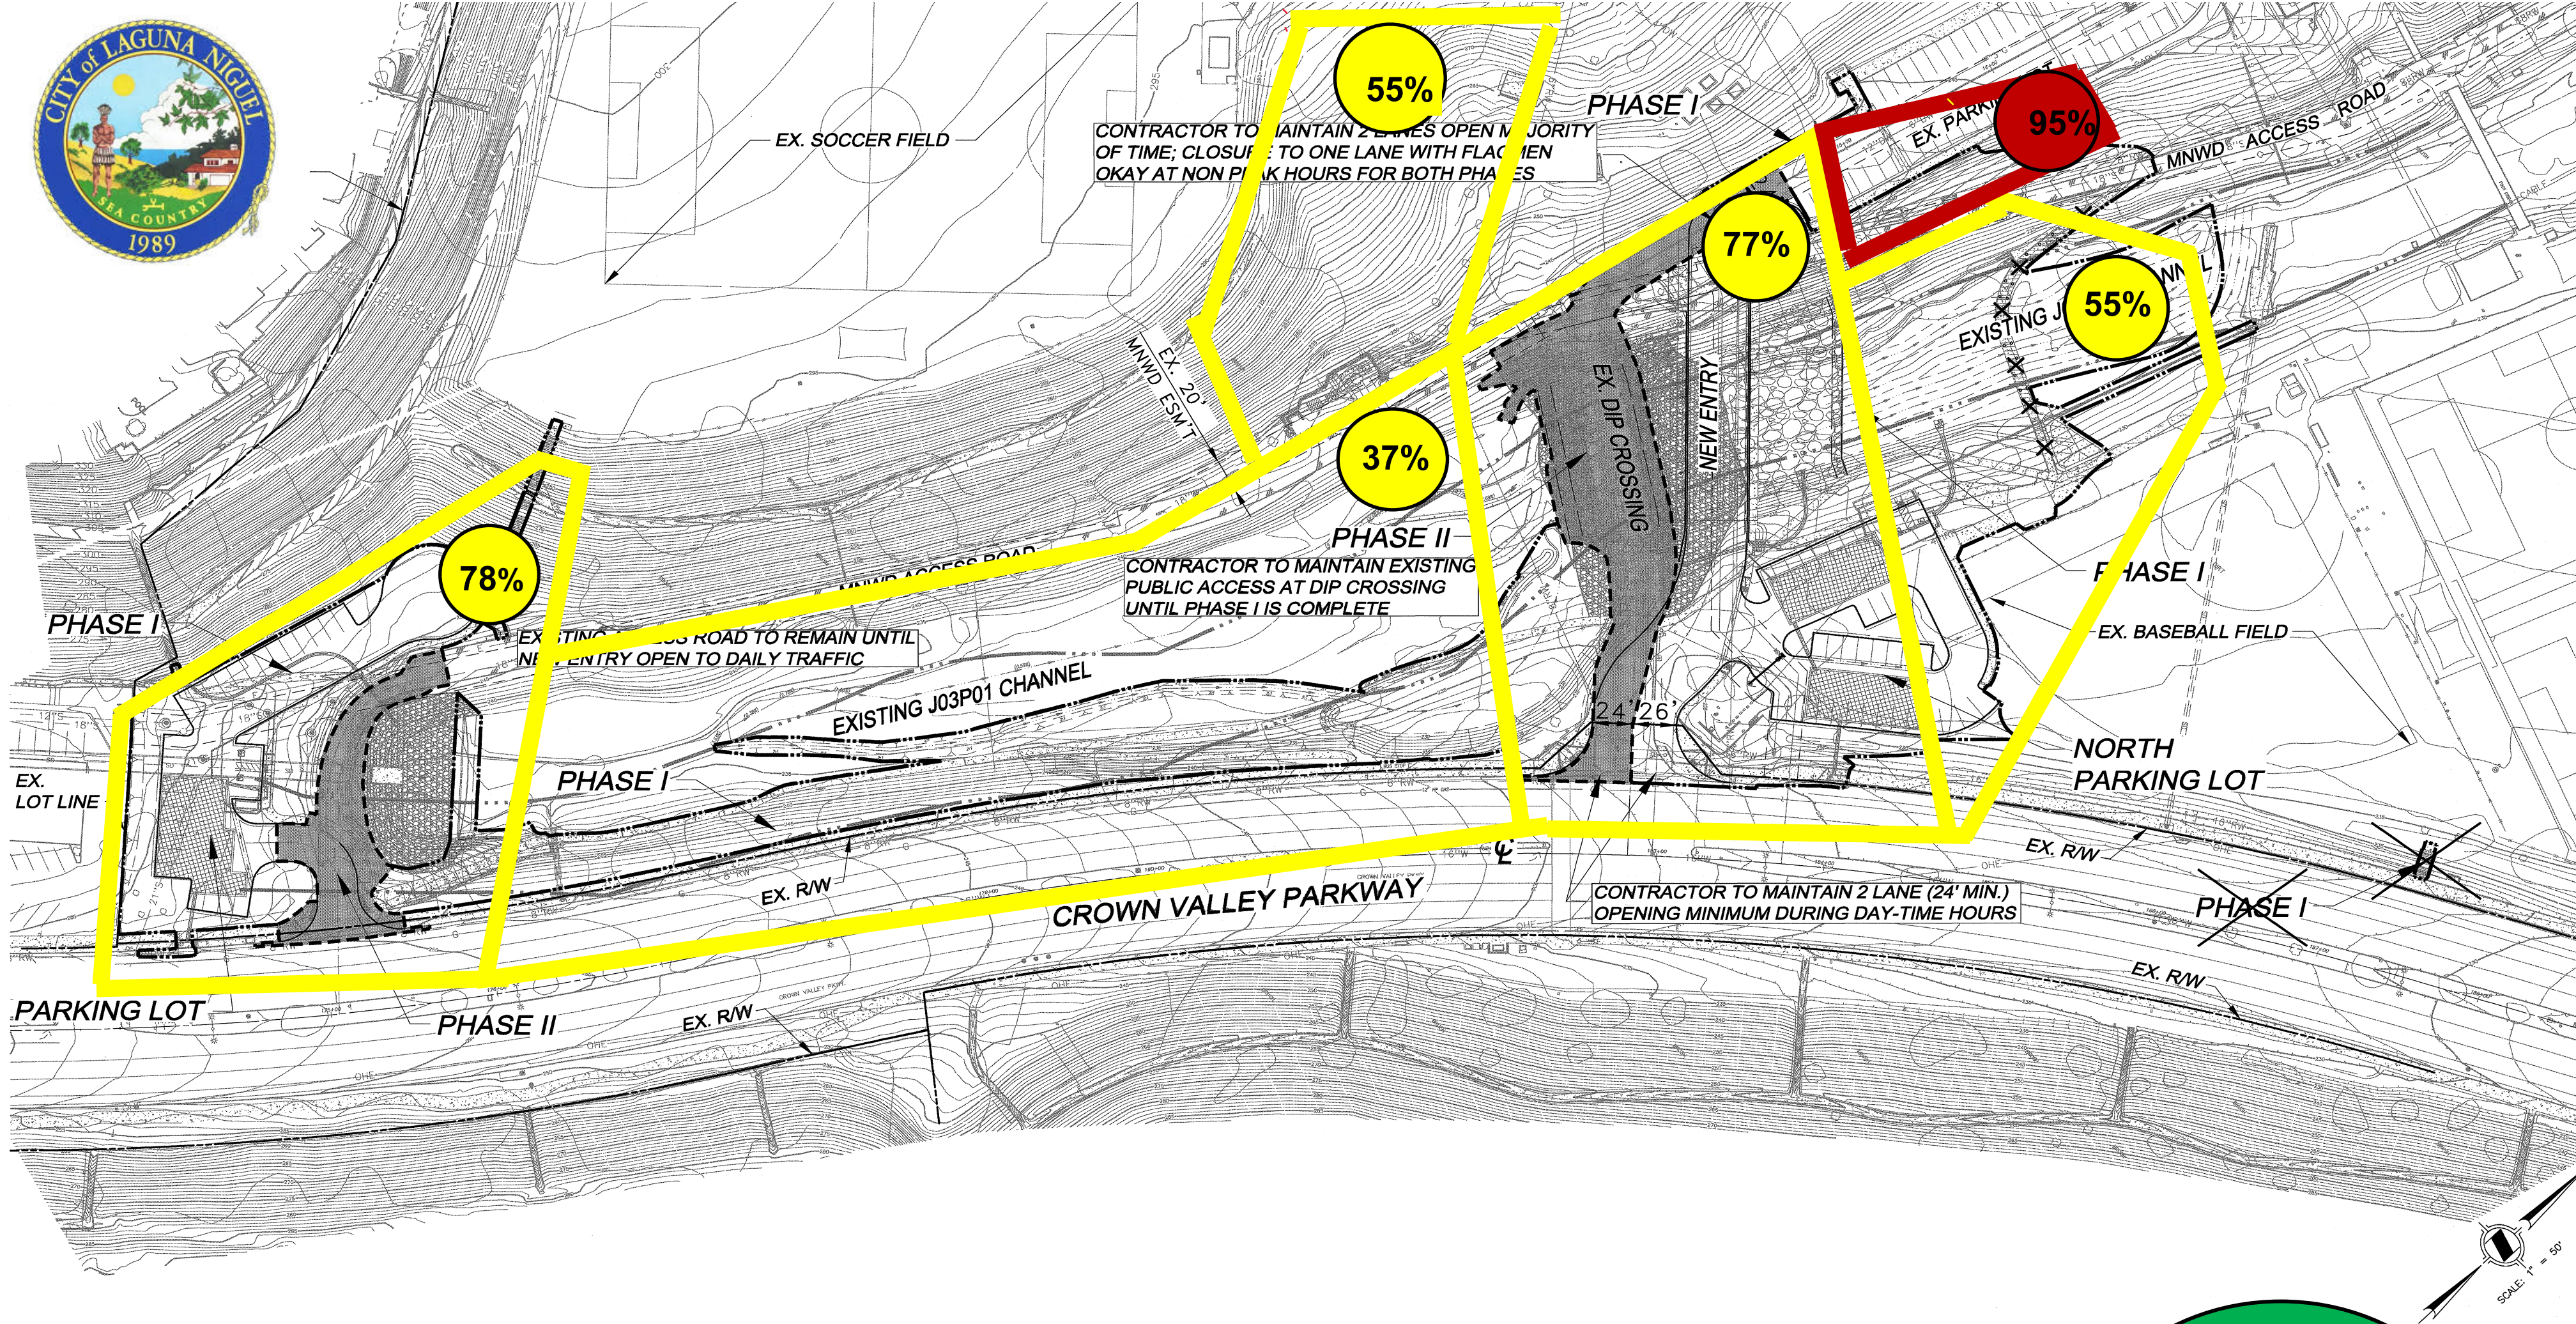

CROWN VALLEY PARK – TIER 2 CONSTRUCTION PROGRESS CHART



CONSTRUCTION PENDING	0% Complete	Construction Start July 5, 2016
CONSTRUCTION UNDERWAY	1% - 99% Complete	 WEEK 42
CONSTRUCTION COMPLETED	100% Complete	Construction Completion June 29, 2017

April 28, 2017

**Your Park is
78.8%
Complete**

SCALE: 1" = 50'
